


Upstream Scenario Modelling Framework

Business Validation

Findings from technical testing, SME review and stakeholder feedback

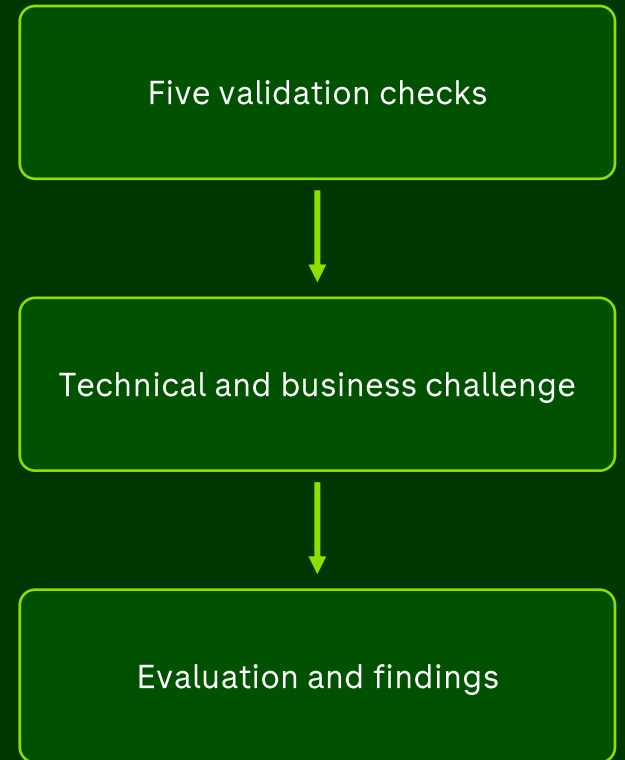

The validation framework approach

Executive Summary

The completed evidence supports the Scenario Modeller’s use for its intended portfolio-planning workflow. The framework reproduced trusted planning structures and profiles, executed controlled scenario operations, integrated manual data and replicated an established A&D case.

✓	PLAN BOOK ACTIVITY REPLICATION Controlled Financial Entity-to-Case mappings and scenario selection reproduced the required Plan Book-aligned oil and gas activity cut.	ACHIEVED
✓	PLAN BOOK METRIC ALIGNMENT Cash Capex and Cash Costs aligned throughout 2026–2035. Production and Post-tax Cash Flow were substantially aligned, with limited and understood variation.	ACHIEVED
✓	OPERATIONS TESTING Seven valid configurations produced the expected transformation, while six invalid configurations returned the expected Home-page validation response.	13 OF 13 PASSED
✓	MANUAL-DATA INTEGRATION All 20 anonymised manual templates flowed through the controlled Teams location and semantic model into the Scenario Modeller.	20 OF 20 INGESTED
✓	A&D DILUTION REPLICATION The modeller reproduced the same financial-profile impact as the established offline A&D dilution case using the equivalent cases, percentage and effective start year.	EXACT ALIGNMENT


4.0 / 5 All three respondents gave the same usability rating.	NPS +67 Forms-calculated overall-success NPS; directional result based on three responses. Targeted stakeholder survey: three respondents; findings are indicative.	3 of 3 Respondents supported further development.
---	--	---

Evidence boundaries • The Plan Book comparison assessed four priority metrics rather than every case-by-year-by-metric combination. • Survey findings are indicative of a targeted three-person expert-user group. • The performance results relate to the current Python-in-Excel implementation and intended Plan Book-aligned workload.	• The testing does not assess enterprise characteristics such as concurrent users, service availability or production infrastructure resilience. • Detailed commercially sensitive profiles and graphical evidence remain in the approved Secret project location.
---	--

Proceed with further development from the validated foundation
The evidence confirms business relevance, controlled execution and technical credibility. Further development should build on the existing modular architecture, extend analytical capability and consider additional processing or interface options as requirements evolve.

Validation Framework

Five controlled tests were combined with stakeholder feedback and technical and business challenge.

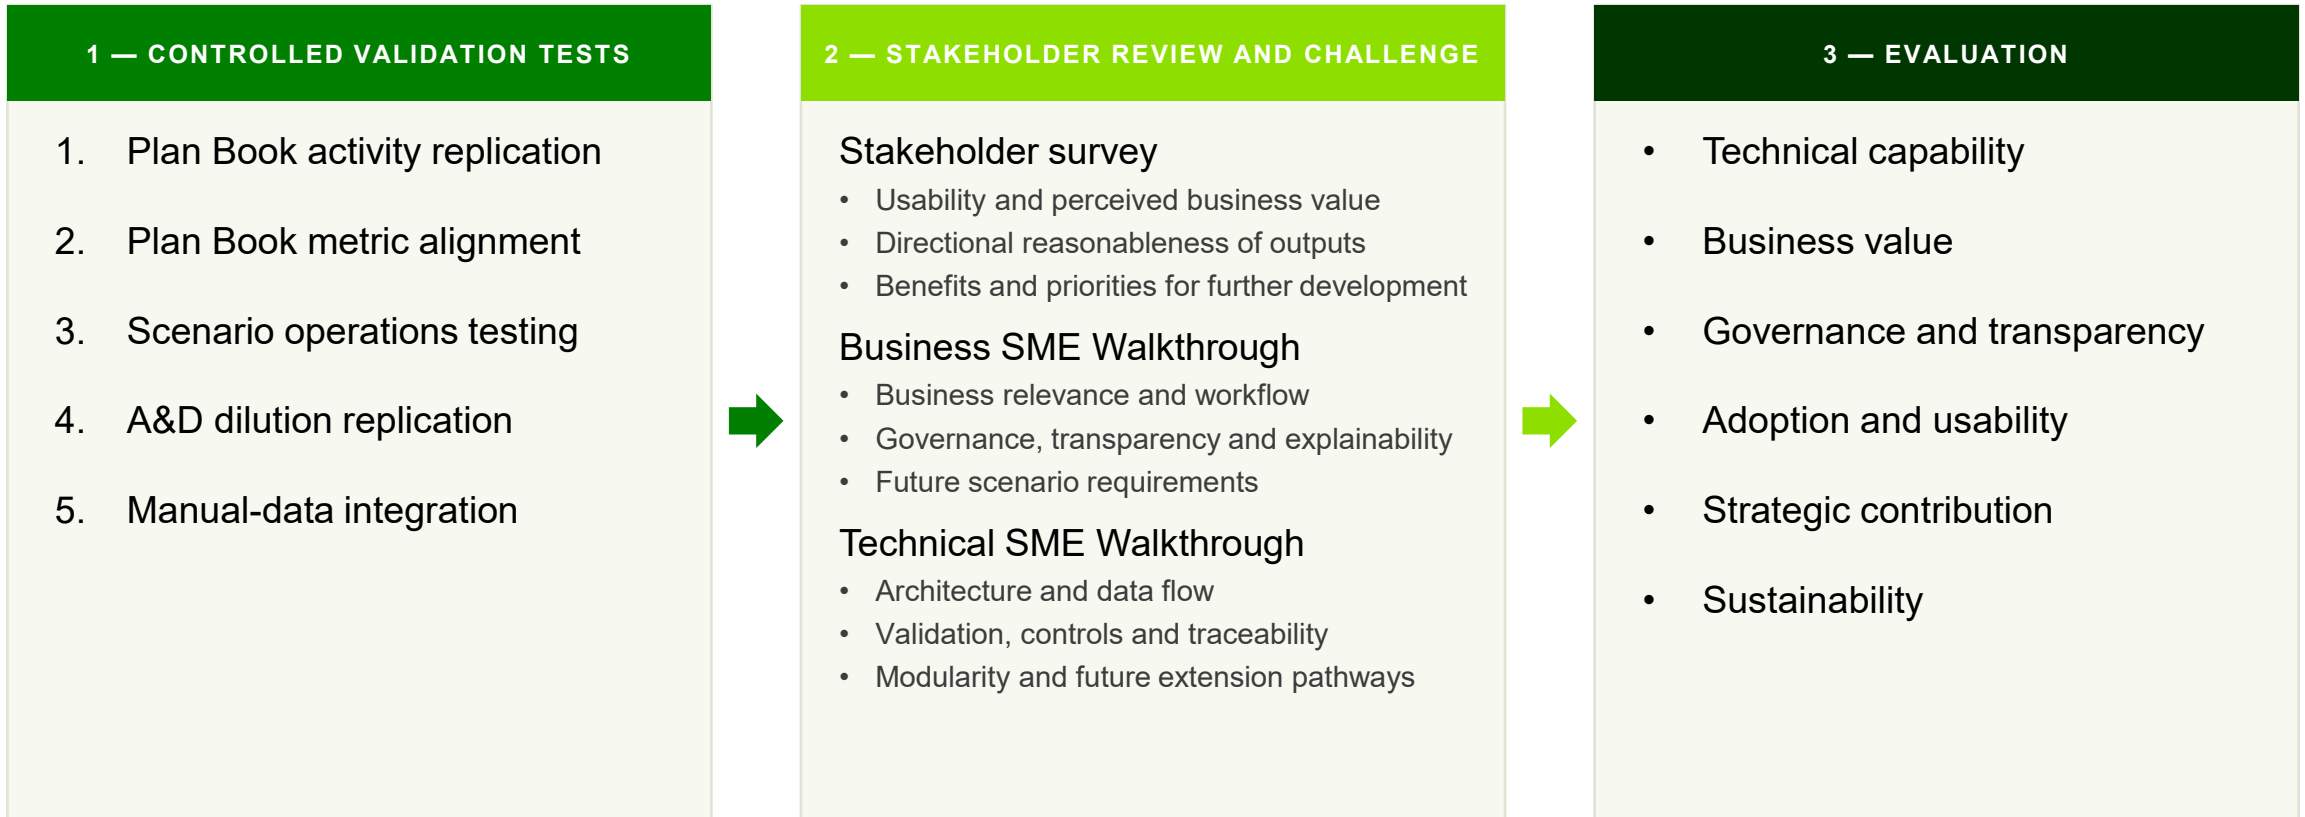

Controlled test evidence → Stakeholder and SME challenge → Balanced evaluation and recommendation

Detailed commercially sensitive profiles, graphical comparisons and operation-level outputs are retained in the approved Secret project location.

Plan Book Replication

Can the modeler, together with the Financial Entity-to-Modelling Case translation input schedule, generate a portfolio activity cut that replicates the Plan Book representation used today?

Finance



Plan Book Replication – Activity Alignment

Can the framework translate financial entities into the same business-facing activity cut used in the Plan Book?

METHOD



MAP

Review the Plan Book structure and assign each financial entity to the appropriate region, country or individual modelling case.



OVERRIDE

Use controlled case-name overrides where financial-entity metadata does not match the business-friendly activity name used in the Plan Book.



SELECT

Configure Scenario 1 to include Main Plan and selected Option cases using No Change.

Unselected SAP options, demonstration-only manual cases, Archaea and Global Gas were excluded to match the selected Plan Book cut.

INTERPRETATION

- Business-facing modelling cases can be created from governed financial-entity metadata using transparent aggregation and override rules.
- Scenario configuration can reproduce the selected planning population without changing the underlying source profiles.

OIL ACTIVITY COMPARISON

Plan Book	Scenario modelling framework		
Oil Regions	Group Entity	Region	Case Name
AGT - ACG	Oil	AGT	AGT
Alaska		AGT Total	
Angola		Alaska	Alaska
BPX Energy		Alaska Total	
Above Area bpx		BPX Energy	Above Area - BPX
Eagle Ford			Eagleford
Haynesville			Haynesville
Permian			Permian
Gulf of America & Canada		BPX Energy Total	
Canada		Gulf of America and Canada	Canada
US - GoA			Above-Area - GoA
Above Area GoA			GoA - Exploration
Exploration			Atlantis
Atlantis			GoA - OBO
GoA OBO			Mad Dog
Mad Dog			Na Kika
Nakika			Paleogene
Paleogene			FE_34413 - Conifer Follow On
Thunder Horse			Thunder Horse
Latin America		Gulf of America and Canada Total	
Argentina		Latin America	Brazil
Brazil		Latin America Total	
MENA - OIL		MENA - OIL	Kirkuk
Middle East - Iraq			Above-Area - Iraq
Kirkuk			Middle East - UAE
Above Area Iraq		MENA - OIL Total	
Middle East - UAE		North Sea	North Sea - UK
North Sea		North Sea Total	
E&I P&O			Central Global Solutions
Region Adjustments			Central Subsurface
RTL			Central Wells
Renewal			Technology
A&D Post Cover			P&O - Overviews and A&D
Divestments			Region Adjustments P&O
Arion			RTL Oil
Chiron			Renewal Oil
Cypress/Sierra			Arion
Frisbee			Chiron
Frisbee II			Cypress/Sierra
Frisbee III			Frisbee
BG Overview			Frisbee II
			Frisbee III
			Business Group Overviews P&O

GAS ACTIVITY COMPARISON

Plan Book	Scenario modelling framework		
Gas Regions	Group Entity	Region	Case Name
AGT - SD	Gas	AGT G&LCE	
Asia Pacific		Asia Pacific	AsPac - Australia
AsPac - Australia			AsPac - Indonesia
AsPac - Indonesia		Asia Pacific Total	
India		India	
Mauritania & Senegal		Mauritania & Senegal	
MENA - G&LCE		MENA - G&LCE	Middle East - Oman
North Africa - Egypt			North Africa - Egypt
North Africa - Libya			North Africa - Libya
Middle East - Oman		MENA - G&LCE Total	
Trinidad		Trinidad	Trinidad
RTL		Trinidad Total	
Renewal		G&LCE - Overviews and A&D	RTL Gas
Gas Organic			Renewal Gas
A&D Post Cover			Bolt
Divestments			Knott
Bolt			Stonefish
Knott / Ver			Alphabet
Stonefish			Heliconia
Access			Sahara
Alphabet			Business Group Overviews Gas
Heliconia			
Sahara			
BG Overview			

Activity replication achieved

The framework recreated the required Plan Book-aligned activity cut while retaining traceability to the underlying financial entities and controlled mapping rules.

Plan Book Replication – Metric Alignment

Can the framework reproduce the shape of the key planning metrics presented in the 2026 O&G LTP Frame?

COMPARISON BASIS

- 1

CONFIGURE
Use the replicated Plan Book activity cut in Scenario 1, with No Change applied to all included cases.
- 2

COMPARE
Compare Scenario Modeller outputs with Ale's 2026 O&G LTP Frame across 2026–2035.
- 3

ASSESS
Review annual profile alignment for Cash Capex, Production, Cash Costs and Post-tax Cash Flow.

This was a focused profile comparison of four priority metrics, not a complete case-by-year-by-metric reconciliation of every Plan Book output.

INTERPRETATION

- All four priority metrics reproduced the expected overall annual profile shape.
- The limited differences were confined to identified years and explained by timing granularity or minor later-year variation.

METRIC PROFILE COMPARISON

METRIC	RESULT	COMPARISON FINDING
Cash Capex	✓ Aligned	Annual profile aligned throughout 2026–2035.
Production	✓ Substantially aligned	Aligned through 2032, with minor variation from 2033–2035.
Cash Costs	✓ Aligned	Annual profile aligned throughout 2026–2035.
Post-tax Cash Flow	✓ Substantially aligned	Slight variation in 2026 and 2027, driven by the Plan Book’s quarterly phasing compared with annual processing in the Scenario Modeller. Aligned from 2028 onward.

Detailed Plan Book and Modeller graph comparisons are retained in the approved Secret project location and are not reproduced in this pack.

Key metric replication achieved

The Scenario Modeller reproduced the annual profile shape of all four priority metrics across 2026–2035. Cash Capex and Cash Costs aligned throughout, while Production and Post-tax Cash Flow were substantially aligned with limited, understood variation.

Operations Testing

Do valid instructions flow through the calculation engine, while invalid instructions stop processing and return a clear error message to the Home page?

Finance




■ What is an operation?

DEFINITION

An operation is a controlled modelling instruction applied to a case profile.

It changes timing, scale, production, cost, CAPEX or transaction assumptions — without manually rebuilding the source profile.

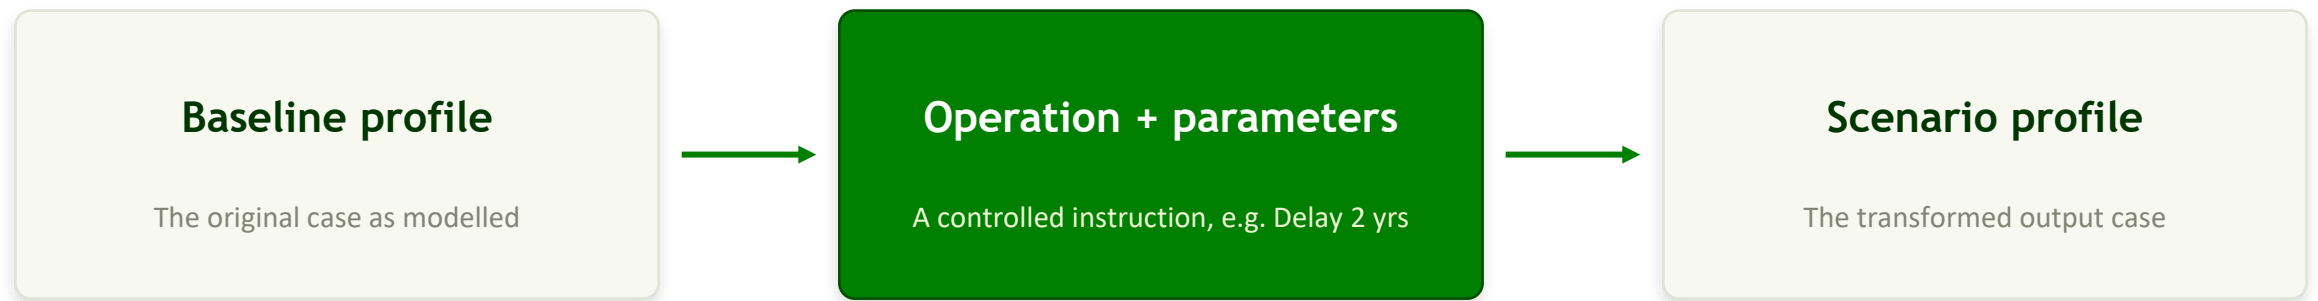

Same source data, applied consistently — no manual profile rebuild.

Operations Testing – Results Overview

Do valid instructions flow through the calculation engine, while invalid instructions stop processing and return a clear error message to the Home page?

TEST METHOD

- 1

ANONYMISED INPUT PROFILES
Load anonymised profiles through the controlled manual-data pathway.
- 2

CONFIGURE OPERATION
Apply the operation to a case using a valid or deliberately invalid entry.
- 3

RUN ENGINE
Execute the scenario run and observe how the engine responds.
- 4

VERIFY OUTPUT OR ERROR
Review the output, or the Home-page error message, against expected behaviour.

Seven operations were assessed through 13 controlled runs: seven expected-success configurations and six expected-error configurations.

TEST OUTCOMES

OPERATION	EXPECTED-SUCCESS TEST	EXPECTED-ERROR TEST	OUTCOME
No Change	Run case as-is	Not applicable	✔ Case passed through unchanged
Delay	Delay by 2 years with a \$100m penalty in 2027	Enter -2 years; the function requires a positive integer	✔ Expected transformation confirmed ✔ Expected error returned
Accelerate	Accelerate by 2 years with \$100m funding in 2027	Enter 2.5 years; the function requires an integer	✔ Expected transformation confirmed ✔ Expected error returned
Farm-in	Increase by 25% from 2028–2035	Reverse the start and end years; start year must precede end year	✔ Expected transformation confirmed ✔ Expected error returned
Farm-down	Decrease by 25% from 2028–2035	Enter 120%; dilution percentage must not exceed 100%	✔ Expected transformation confirmed ✔ Expected error returned
Production Change	Increase by 25% from 2028–2035	Reverse the start and end years; start year must precede end year	✔ Expected transformation confirmed ✔ Expected error returned
Cost Change	Add \$100m in 2030	Remove the year input; each value requires a corresponding year	✔ Expected transformation confirmed ✔ Expected error returned

The results confirm both sides of the operational control: the engine applies valid scenario instructions correctly and prevents invalid parameter combinations from being processed silently.

13/13
CONTROLLED RUNS

13 of 13 controlled runs produced the expected outcome

Valid configurations flowed through the engine and produced the expected profile behaviour. Deliberately invalid configurations stopped processing and returned a clear validation message to the Home page.

Operations Testing – Evidence Success Cases

Scenario configuration inputs – how the test case were configured in the scenario modelling framework

Case Information			Operation		Operation input 1			Operation Input 2			Operation Input 3		
Case name, Segment, Region, Country reference data and current Plan Type			Choose whether to include or exclude a case, then choose an operation to apply										
Locked Cells Input Cells													
Case ID	Case Name	Included (y/n	Choose Operation	Operation Description	Input 1 Label	Input 1 Required	Input 1	Input 2 Label	Input 2 Required	Input 2	Input 3 Label	Input 3 Required	Input 3
1	Project Golden Dune	Yes	No Change	Retains profile unchanged	n/a	-		n/a	-		n/a	-	
2	Project Sandpiper	Yes	Delay	Moves profile later	Yrs to delay (whole number)	Yes	2	Delay penalty (\$m)	Optional	100	Penalty year	Optional	2027
3	Project Frontier West	Yes	Accelerate	Moves profile earlier	Yrs to accelerate (whole number)	Yes	2	Funding required (\$m)	Optional	100	Funding year	Optional	2027
4	Project Crimson Basin	Yes	Farm In (Increase)	Increases selected profile	Increase % (as fraction)	Yes	0.25	Effective start year	Optional	2028	Effective end year	Optional	2035
5	Project Deepstone	Yes	Farm Down (Dilution)	Reduces selected profile	Dilution % (as fraction)	Yes	0.25	Effective start year	Optional	2028	Effective end year	Optional	2035
6	Project Phoenix Recovery	Yes	Production Change %	Adjusts production by a %	% change (as fraction)	Yes	0.25	Start year	Optional	2028	End year	Optional	2035
7	Project Neptune Expansion	Yes	CAPEX Change \$m	Adjusts CAPEX by \$m	Change Yr1 (± \$m)	Yes	100	Year 1	Yes	2030	Change Yr2 (± \$m)	Optional	

Case test results – output tables produced for each test case

Case 1 – profile remains unchanged as expected

Value \$bn		Year									
Scenario Name	ID	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035
(S1) Operation testing	1	5.7	4.3	4.0	4.2	4.0	3.8	3.7	3.6	3.4	3.3
(S2) Reference case	1	5.7	4.3	4.0	4.2	4.0	3.8	3.7	3.6	3.4	3.3
Grand Total		11.3	8.5	8.1	8.5	8.1	7.5	7.4	7.1	6.9	6.6

Case 2 – profile delayed 2 years, with \$100m penalty in 2027 impacting target metrics cash costs and underlying RCOP

Sum of Value		Year									
Scenario Name	Metric	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035
(S1) Operation testing	Total Cash Costs		-100	-270	-270	-250	-250	-250	-250	-250	-250
	Underlying RCOP		-100	390	230	300	300	310	300	300	290
(S2) Reference case	Total Cash Costs	-270	-270	-250	-250	-250	-250	-250	-250	-250	-250
	Underlying RCOP	390	230	300	300	310	300	300	290	290	280
Grand Total		120	-240	170	10	110	100	110	90	90	70

Case 3 – profile accelerated 2 years, with \$100m funding in 2027 impacting target metrics cash capex and pre-tax cash flow

Sum of Value		Year									
Scenario Name	Metric	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035
(S1) Operation testing	Cash Capex	-500	-530	-410	-400	-360	-310	-300	-270	-230	-190
	Pre Tax Cash Flow	380	320	400	370	380	380	370	360	350	330
(S2) Reference case	Cash Capex	-480	-480	-500	-430	-410	-400	-360	-310	-300	-270
	Pre Tax Cash Flow	600	370	380	420	400	370	380	380	370	360
Grand Total		0	-320	-130	-40	10	40	90	160	190	230

Case 4 – profile increased by 25% for years 2028 to 2035 only

Sum of Value	Year											
Scenario Name	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037
(S1) Operation testing	600	370	475	525	500	462.5	475	475	462.5	450	350	330
(S2) Reference case	600	370	380	420	400	370	380	380	370	360	350	330
Grand Total	1200	740	855	945	900	832.5	855	855	832.5	810	700	660

Change 0% 0% 25% 25% 25% 25% 25% 25% 25% 25% 0% 0%

Case 5 – profile decreased by 25% for years 2028 to 2035 only

Sum of Value	Year											
Scenario Name	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037
(S1) Operation testing	600	370	285	315	300	277.5	285	285	277.5	270	350	330
(S2) Reference case	600	370	380	420	400	370	380	380	370	360	350	330
Grand Total	1200	740	665	735	700	647.5	665	665	647.5	630	700	660

Change 0% 0% -25% -25% -25% -25% -25% -25% -25% -25% 0% 0%

Case 6 – production and impacted metrics increased by 25% for years 2028 to 2035 only

Sum of Value		Year										
Scenario Name	Metric	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036
(S1) Operation testing	Total Production (mboed)	30	40	50	50	50	37.5	37.5	37.5	37.5	37.5	20
(S2) Reference case	Total Production (mboed)	30	40	40	40	40	30	30	30	30	30	20
Grand Total		60	80	90	90	90	67.5	67.5	67.5	67.5	67.5	40

0% 0% 25% 25% 25% 25% 25% 25% 25% 25% 25% 0%

Sum of Value		Year										
Scenario Name	Metric	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036
(S1) Operation testing	DD&A Charge	-610	-690	-875	-825	-787.5	-737.5	-700	-637.5	-612.5	-587.5	-430
	Total Cash Costs	-270	-270	-312.5	-312.5	-312.5	-312.5	-312.5	-312.5	-312.5	-312.5	-250
	Gross Margin	1340	1180	1550	1500	1462.5	1412.5	1375	1300	1275	1237.5	930
(S2) Reference case	DD&A Charge	-610	-690	-700	-660	-630	-590	-560	-510	-490	-470	-430
	Total Cash Costs	-270	-270	-250	-250	-250	-250	-250	-250	-250	-250	-250
	Gross Margin	1340	1180	1240	1200	1170	1130	1100	1040	1020	990	930
Grand Total		920	440	652.5	652.5	652.5	652.5	652.5	630	630	607.5	500

0% 0% 25% 25% 25% 25% 25% 25% 25% 25% 25% 0%
0% 0% 25% 25% 25% 25% 25% 25% 25% 25% 25% 0%
0% 0% 25% 25% 25% 25% 25% 25% 25% 25% 25% 0%

Case 7 – \$100m added to cash capex in 2030 only

Sum of Value		Year										
Scenario Name	Metric	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	
(S1) Operation testing	Cash Capex	-480	-480	-500	-430	-510	-400	-360	-310	-300	-270	
(S2) Reference case	Cash Capex	-480	-480	-500	-430	-410	-400	-360	-310	-300	-270	
Grand Total		-960	-960	-1000	-860	-920	-800	-720	-620	-600	-540	

Operations Testing – Evidence Error Cases

Case 2: Setting delay years to -2 in delay operation inputs

✗ Scenario engine run failed.

Scenario S1 could not process 'Project Sandpiper ' (ID 2) using operation 'Delay'. Review the scenario configuration and run the engine again.

- Scenario: S1
- Case: Project Sandpiper (ID 2)
- Operation: Delay
- Error: Delay years must be zero or a positive whole number.

Case 5: Setting dilution percentage to 120% in farm-down operation inputs

✗ Scenario engine run failed.

Scenario S1 could not process 'Project Deepstone ' (ID 5) using operation 'Dilution'. Review the scenario configuration and run the engine again.

- Scenario: S1
- Case: Project Deepstone (ID 5)
- Operation: Dilution
- Error: Dilution percentage must be between 0 and 1 inclusive.

Case 3: Setting accelerate years to 2.5 in accelerate operation inputs

✗ Scenario engine run failed.

Scenario S1 could not process 'Project Frontier West ' (ID 3) using operation 'Accelerate'. Review the scenario configuration and run the engine again.

- Scenario: S1
- Case: Project Frontier West (ID 3)
- Operation: Accelerate
- Error: Acceleration years must be entered as a whole number.

Case 6: Swapping start and end year in production change operation inputs

✗ Scenario engine run failed.

Scenario S1 could not process 'Project Phoenix Recovery ' (ID 6) using operation 'ProdnAdj'. Review the scenario configuration and run the engine again.

- Scenario: S1
- Case: Project Phoenix Recovery (ID 6)
- Operation: ProdnAdj
- Error: Production adjustment start year cannot be after the end year.

Case 4: Swapping start and end year in farm-in operation inputs

✗ Scenario engine run failed.

Scenario S1 could not process 'Project Crimson Basin ' (ID 4) using operation 'Increase'. Review the scenario configuration and run the engine again.

- Scenario: S1
- Case: Project Crimson Basin (ID 4)
- Operation: Increase
- Error: Farm-in start year cannot be after the end year.

Case 7: Removing the year input in capex change operation inputs

✗ Scenario engine run failed.

Scenario S1 could not process 'Project Neptune Expansion ' (ID 7) using operation 'CapexAbsolute'. Review the scenario configuration and run the engine again.

- Scenario: S1
- Case: Project Neptune Expansion (ID 7)
- Operation: CapexAbsolute
- Error: Each CAPEX adjustment requires both an adjustment amount and an adjustment year.

Manual Input Integration

Can standardised manual profiles be stored securely,
ingested through the semantic model and made available
correctly within the Scenario Modeller?

Finance



Manual Input Integration

Can standardised manual profiles be stored securely, ingested through the semantic model and made available correctly within the Scenario Modeller?

STANDARDISED INPUT

Anonymised profile data entered through the controlled manual-input template.

The schedule captures required case metadata and annual financial-profile values in a consistent structure.

<

Secure Teams location

2026 LTP													
Posts Shared Data Sourcing and Tra...													
> Data Inputs > LTP_Manual_Feeds													
Unsaved changes													
All Documents + Add view													
Name													
Standardised Input Template.xlsx													
Standardised Input Template 9.xlsx													
Standardised Input Template 8.xlsx													
Standardised Input Template 7.xlsx													
Standardised Input Template 6.xlsx													
Standardised Input Template 5.xlsx													
Standardised Input Template 4.xlsx													
Standardised Input Template 3.xlsx													
Standardised Input Template 2.xlsx													
Standardised Input Template 10.xlsx													

Semantic model ingestion

SCENARIO MODELLER

All cases become available alongside system-sourced cases for controlled scenario selection and processing.

The imported cases retained their case name, segment, region, country and Manual plan-type classification.

Upstream Scenario Modelling Framework Scenario Configuration													
Home S1 S2 S3 S4 S5 Results Help													
Scenario Name All data for testing													
Description													
Last Updated													
Configured By													
Configure a scenario by selecting planning cases to include or exclude and applying operations that modify timing, scale or input values to evaluate alternative outcomes.													
Case Information													
Case name, Segment, Region, Country reference data and current Plan Type													
Locked Cells Input Cells													
Case ID	Case Name	Segment	Region	Country	Plan Type								
1	Project Golden Dune	G&LC	Asia Pacific	AsPac - Australia	Manual								
2	Project Sandpiper	G&LC	India	India	Manual								
3	Project Frontier West	G&LC	MENA - G&LCE	North Africa - Egypt	Manual								
4	Project Crimson Basin	G&LC	Trinidad	Trinidad	Manual								
5	Project Deepstone	P&O	AGT	AGT - Azerbaijan	Manual								
6	Project Phoenix Recovery	P&O	BPX Energy	BPX	Manual								
7	Project Neptune Expansion	P&O	Gulf of America and Canada	US - GoA	Manual								
8	Project Falcon Ridge	P&O	Latin America	Argentina	Manual								
9	Project Northern Horizon	P&O	MENA - OIL	Middle East - Iraq	Manual								
10	Project Blackwater	P&O	North Sea	North Sea - UK	Manual								

Manual-data integration achieved

All 20 anonymised manual templates were securely stored, ingested through the semantic model and returned successfully within the Scenario Modeller.

Manual-data integration test. Anonymised test profiles were used throughout; no live business data is shown.


A&D Dilution Replication

Can the framework recreate an existing A&D case that has previously been modelled offline as a dilution, avoiding the need to manually create a separate adjusted profile?

Finance

A&D Dilution Replication

Validation tested whether the same financial-profile impact could be produced without manually creating and loading a separate adjusted case.



SCREENSHOT 1 – CONFIGURATION



The equivalent cases were brought together in the modeller and configured using the required dilution percentage and effective start year.

A&D Case Replicated Exactly

Test passed: the modeller reproduced the same financial-profile impact as the established offline A&D case.

The result demonstrates that the dilution can be generated directly from the underlying asset cases, avoiding the need to manually create, load and maintain a separate adjusted profile.

SCREENSHOT 2 – OUTPUT COMPARISON

Upstream Scenario Modelling Framework Results																
Home 1 S1 2 S2 3 S3 4 S4 5 S5 Results i Help																
Segment	All															
Operation	All															
Scenario	All															
Plan Type	All															
Metric	Cash Capex															
Group Entity	All															
Region	All															
Country	All															
Sum of Value		Year														
Scenario Name	Case Name	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	2038	2039	2040	Grand Total	
Redacted		(1,618)	(1,119)	(717)	(344)	(65)	(206)	(193)	(42)	(98)	(70)	(16)	(121)	(164)	(4,772)	
		(1,618)	(1,119)	(717)	(344)	(65)	(206)	(193)	(42)	(98)	(70)	(16)	(121)	(164)	(4,772)	

The model-generated profile aligned exactly with the existing A&D financial-entity profile created through the offline method and loaded through SAP.

Repeatability – Controlled percentage and effective-year inputs

Consistency – Aligned with the established A&D case

Traceability – Adjustment linked to selected underlying cases

Efficiency – Removes separate offline profile preparation

Stakeholder Survey

Does structured feedback from users and stakeholders support the expected benefits around effort reduction, consistency, traceability, usability, governance, and decision support?

Finance

Stakeholder testing supported that the framework produced understandable and expected scenario outcomes

Questions 1–7 assessed the relevance of the respondent group, the perceived operation of the framework and its potential effect on modelling effort.

These questions establish whether feedback came from relevant users and whether the framework behaved as expected when applied to scenario-modelling requirements.

RESPONDENT CONTEXT

Roles represented

- PPM – 1
- Data & Analytics – 1
- Digital Transformation – 1


Previous scenario-modelling experience

- Yes – 2
- Some involvement – 1
- No – 0

The survey brought together complementary planning, analytical and transformation perspectives. All respondents had either direct scenario-modelling experience or some prior involvement.


EFFORT SAVING EXPECTED (Q7)

Expected reduction in scenario-preparation effort



FRAMEWORK ASSESSMENT (Q1–7)

This question tested whether the framework addressed its central design objectives across usability, efficiency, governance, traceability and decision support.

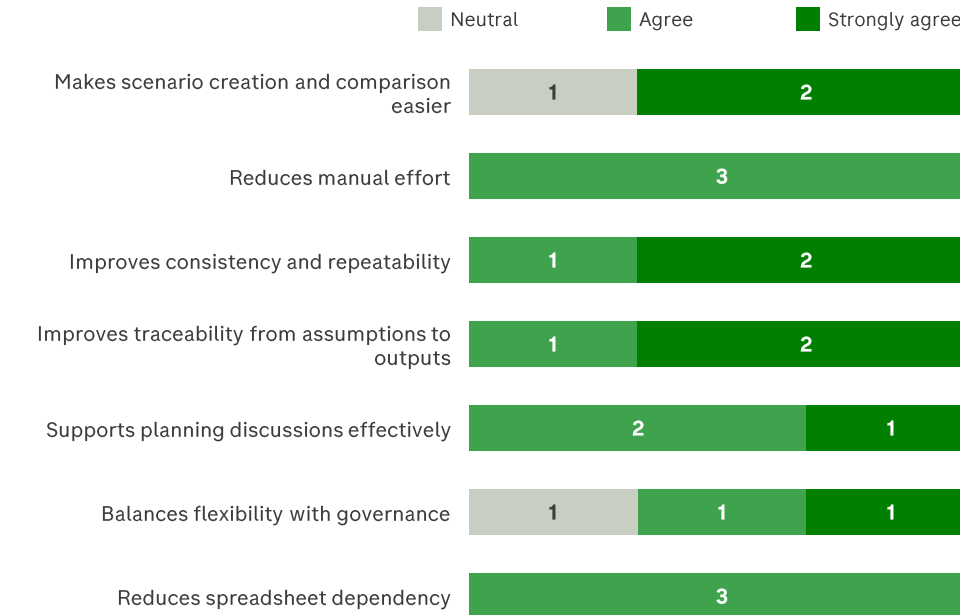


Responses were predominantly positive across all seven statements. The strongest evidence related to consistency, repeatability and traceability. Neutral responses on ease of scenario comparison and the balance between flexibility and governance indicate areas where further refinement may strengthen the user experience.

OUTPUT VALIDATION (Q4–5)

These questions tested business reasonableness: whether the modelled changes were represented correctly and whether the resulting profile direction aligned with stakeholder expectations.

Q4 Outputs directionally consistent with expectations



3 of 3

Confirmed requested changes were represented

All respondents confirmed that the requested scenario changes were represented successfully. Two considered the outputs fully directionally consistent and one selected 'Mostly'.

No responses were submitted to the optional explainability question (Q6); no conclusion has therefore been drawn from this item.

Stakeholder testing supports the functional validity of the framework: requested changes were represented successfully, outputs were directionally credible, and respondents generally recognised improved consistency, traceability and efficiency.


■ Respondents recognised broad business value and unanimously supported further development

Questions 8–15 assessed benefits, usability, overall success and priorities for the next stage.

These questions tested whether the prototype created relevant business value, was usable by its intended audience and provided sufficient evidence to justify continued development.

BENEFITS DELIVERED (Q8)

Benefits selected by respondents – tested whether the prototype delivered against the business problems it was designed to address.

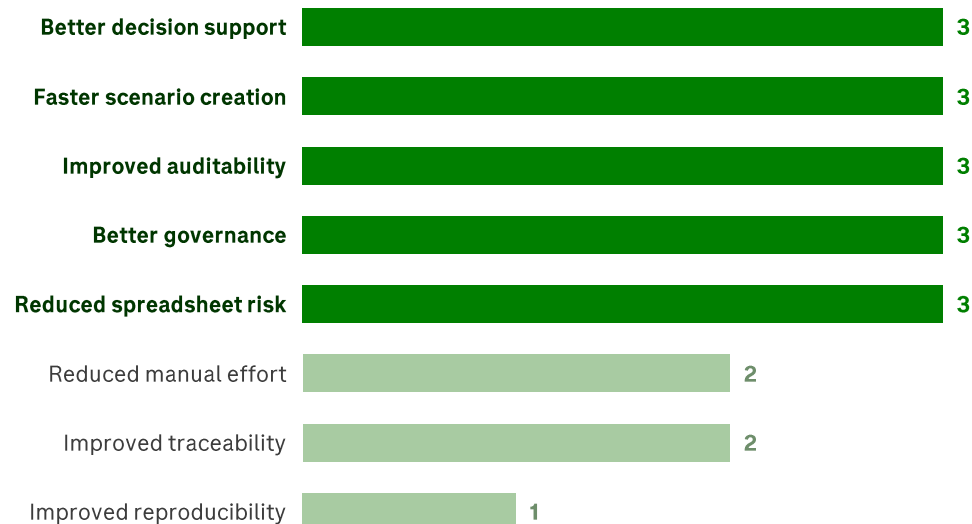

The most consistently recognised benefits extended beyond speed. All respondents identified decision support, auditability, governance and spreadsheet-risk reduction, indicating that the perceived value lies in both analytical efficiency and stronger control.

"An excellent tool that takes a complex and highly specific processes that are currently executed manually, and brings them together into an automated and effective modelling framework."

Survey respondent

"Further enhancement to web-based application will completely eliminate the excel dependencies"

Survey respondent

4.0 / 5

Usability rating (Q9)
All three respondents rated
usability 4 out of 5

NPS +67

Forms-calculated overall-
success NPS

3 of 3

Support further development

NPS distribution – Promoters 2 | Passives 1 | Detractors 0. Based on three responses, treat as a directional stakeholder indicator rather than a statistically representative benchmark.

FUTURE-DEVELOPMENT PRIORITIES (RANKED)

- | | |
|--|--|
| 1 Automation of scenario creation and comparison | 5 Automated scenarios through an optimisation engine |
| 2 Investment ratios such as NPV, IRR and related metrics | 6 User experience and ease of use |
| 3 Governance, controls and auditability | 7 Reporting and visualisation improvements |
| 4 Integration with existing planning data and tools | 8 Other |

Respondents prioritised deeper automation and investment-decision metrics while continuing to value governance and integration. The next stage should extend analytical capability without weakening control or traceability.

Support for further development was unanimous. No concerns or preconditions were submitted through the survey; this is not evidence that none exist.

The comments reinforce both sides of the conclusion: the prototype consolidates complex manual activity, while a future web-based implementation is seen as an opportunity to reduce the remaining Excel dependency.

The survey provides positive evidence across business value, usability and adoption: respondents recognised benefits in automation, governance and decision support, rated usability consistently at 4/5, produced a positive NPS of +67 and unanimously supported further development.

SME Walkthroughs

Summaries of the business and technical SME walkthrough sessions, covering key topics, questions raised, and feedback provided.

Finance



SME reviews confirmed the framework's business value and technical strength

Business and technical walkthroughs validated a governed, transparent and extensible scenario-modelling capability.



Business review: valuable, controlled and understandable

Business SME Walkthrough — 10 August 2026

WHAT WAS DEMONSTRATED

- Controlled translation from financial entities to modelling cases
- Governed manual inputs and configurable scenario operations
- Validation, error guidance and scenario-output analysis

KEY BUSINESS DISCUSSION

- Maintaining transparency while retaining essential SME judgement
- Governing source refreshes, manual inputs and scenario history
- Extending the operations library to future ownership-change requirements

WHAT WAS LEARNED

The review confirmed that the framework converts specialist scenario activity into a more transparent, repeatable and auditable workflow. Stakeholders understood the approach, recognised its value and identified relevant opportunities for continued enhancement.

“Wonderful application” — Business walkthrough participant



Technical review: governed, modular and extensible

Technical SME Walkthrough — 11 August 2026

WHAT WAS DEMONSTRATED

- Governed integration across enterprise data, Power BI, Excel and Python
- Modular scenario operations with structured validation and error handling
- Traceable execution, runtime logging and interactive output analysis

ARCHITECTURE EVOLUTION DISCUSSION

- ↑ Opportunity to move additional processing upstream as requirements and platform capability develop
- ↑ Opportunity to introduce alternative interfaces while retaining flexible Excel analysis

WHAT WAS LEARNED

The review confirmed that the current architecture provides a credible and effective foundation for the planning workflow. Its governed data integration, modular Python engine and familiar user interface support both current use and future extension.

BUSINESS VALUE CONFIRMED

- Stakeholders understood the workflow and recognised its relevance to portfolio planning.

CONTROLS DEMONSTRATED

- Governed inputs, explicit validation and traceable execution were evidenced.

EXTENSIBLE FOUNDATION

- The modular design supports additional operations, processing options and interfaces as requirements develop.

The SME reviews confirmed the framework as a credible, governed and extensible scenario-modelling capability that improves transparency, repeatability and control within the intended planning workflow.

Overall Evaluation and Recommendation

The evidence supports the Scenario Modeller as a credible, governed and extensible capability for the intended planning workflow.

The framework reproduced trusted planning structures and profiles, executed controlled operations, integrated manual data and provided outputs that stakeholders could understand, review and challenge.

Evaluation dimension	Assessment	Evidence-based conclusion
Technical capability	✓ Supported	Completed Plan Book, operations, manual-integration, A&D and performance testing demonstrated controlled end-to-end execution.
Business value	✓ Supported	The framework reproduced established planning outcomes and respondents recognised benefits in scenario speed, decision support, auditability and governance.
Governance and transparency	✓ Supported	Controlled mappings, standardised inputs, visible assumptions, validation messages and traceable execution strengthen the scenario process.
Adoption and usability	● Positive targeted evidence	All three respondents rated usability 4 out of 5 and supported further development; SME walkthroughs confirmed that the workflow and outputs were understandable.
Strategic contribution	✓ Supported	The framework provides a reusable capability for creating, comparing and explaining portfolio scenarios through consistent rules and controlled inputs.
Sustainability	◆ Extensible foundation	The modular Python engine, governed data model and familiar Planning interface provide a strong basis for additional operations, processing options and interfaces.

Recommendation: proceed with further development from the validated foundation
